Activity ID	Activity Description
SITE SELECTION / AUTHORIZATION	
A0001	SITE EVALUATION
A0005	AUTHORIZATION TO PROCEED
PERMITTING	
A0025	PREPARE PSD PERMIT APPLICATION
A0030	AGENCY REVIEW PSD APPLICATION
A0031	PREPARE OTHER PERMIT APPLICATIONS
A0034	AGENCY REVIEW OTHER APPLICATIONS
A0035	OBTAIN CONSTRUCTION PERMITS
ENGINEERING / PROCUREMENT	
A0045	GA / SITE DEVELOPMENT / PLANT PERFORMANCE
A0046	FINALIZE CYCLE & PREPARE MAJOR SPECIFICATIONS
A0047	PROCURE STEAM GENERATOR
A0047M	AWARD STEAM GENERATOR
A0048	FABRICATE/ DELIVER STEAM GENERATOR
A0050	PROCURE TURBINE GENERATOR
A0050M	AWARD TURBINE GENERATOR
A0051	FABRICATE / DELIVER TURBINE GENERATOR
A0052	PROCURE FGD SYSTEM
A0053	FABRICATE / DELIVER FGD SYSTEM
A0056	PROCURE MATERIAL HANDLING SYSTEM
A0057	FABRICATE / DELIVER MATERIAL HANDLING SYS
A0058	PROCURE GEOTECH SERVICES CONTRACTOR
A0059	GEOTECH TESTING / REPORT
A0060	PROCURE MAJOR EQUIPMENT
A0067	P&ID DEVELOPMENT
A0068	FINALIZE GAs / START DETAILED DESIGN
A0070	POWER BLOCK SUBSTRUCTURE DESIGN
A0072	POWER BLOCK STR. STEEL DESIGN/FAB/DELV
A0073	BOILER ROOM STRUCTURAL STEEL MILL ORDER
A0074	BOILER ROOM STRUCTURAL STEEL FAB RELEASE
A0076	WIRING DESIGN
A0078	CRITICAL PIPE DESIGN
CONSTRUCTION	
A0084	PROCURE SITE CLEARING CONTRACTOR
A0085	SITE CLEARING & ACCESS
A0086	SITEWORK
A0087	POWER BLOCK SUBSTRUCTURE
A0090	POWER BLOCK STRUCTURAL STEEL
A0115	BOILER PRESSURE PARTS
A0117	RAISE STEAM DRUM
A0125	BOILER HYDRO TEST
A0127	BOILER INSULATION & TRIM
A0137	TURBINE GENERATOR
A0140	CHIMNEY SHELL
A0141	CHIMNEY LINER
A0142	FGD / BAGHOUSE
A0145	MATERIAL HANDLING SYSTEM
STARTUP & TESTING	
A0160	ENERGIZE SWITCHGEAR
A0170	MATERIAL HANDLING SYSTEM CHECKOUT
A0175	BOILOUT / STEAM BLOW / RESTORE
A0180	UNIT INITIAL OPERATION
A0185	COMMERCIAL OPERATION - UNIT 1
A0190	COMMERCIAL OPERATION - UNIT 2

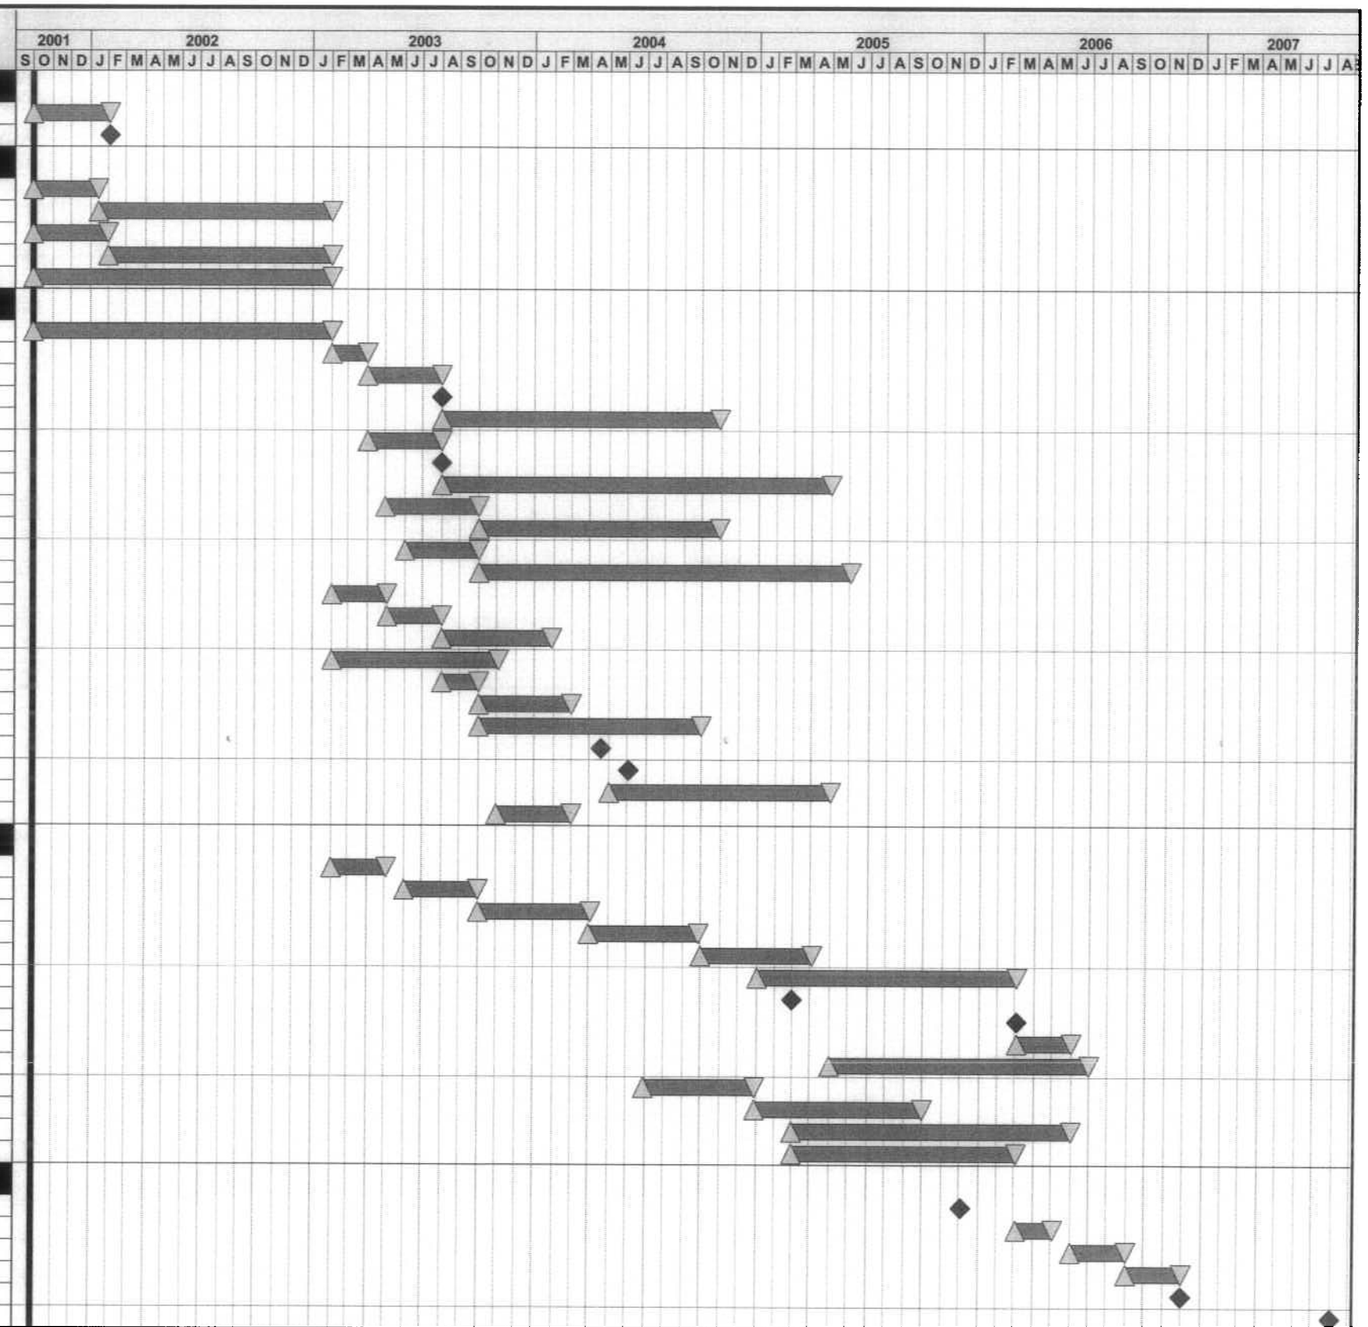

Run Date 16OCT02 16:07

Figure 2-7

© Primavera Systems, Inc.

C395

ROUNDUP

Sheet 1 of 1

PROJECT SCHEDULE
390 GROSS MW x 2 - PULVERIZED COAL PLANT
START ENGINEERING/PROCUREMENT AFTER PERMIT

Sargent & Lundy LLC
